
Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float
RC2-SAMPLE Riverside College Stage 2 (Sample)		289	289	0%	01-Feb-27	07-Apr-28	0
RC2-SAMPLE.1 Key Milestones		289	289	0%	01-Feb-27	07-Apr-28	0
A1000	Contract award / site possession	0	0	100%	01-Feb-27		0
A1030	Practical completion - whole of works	0	0	0%		07-Apr-28	0
RC2-SAMPLE.2 Preliminaries & Approvals		289	289	0%	01-Feb-27	07-Apr-28	0
A1040	Site establishment, hoarding & amenities	10	10	0%	01-Feb-27	12-Feb-27	0
A1060	Construction management plan & traffic management	10	10	0%	01-Feb-27	12-Feb-27	0
A1100	Site demobilisation	10	10	0%	27-Mar-28	07-Apr-28	0
RC2-SAMPLE.4 Site Works & In-ground Services		25	25	0%	15-Feb-27	19-Mar-27	0
A1300	Demolition of existing transportables	10	10	0%	15-Feb-27	26-Feb-27	0
A1310	Bulk earthworks & site cut	15	15	0%	01-Mar-27	19-Mar-27	0
RC2-SAMPLE.5 Building A - Classroom Block (2 levels)		164	164	0%	22-Mar-27	11-Nov-27	0
RC2-SAMPLE.5.1 Substructure		44	44	0%	22-Mar-27	26-May-27	0
A1360	Bored piers	12	12	0%	22-Mar-27	08-Apr-27	0
A1370	Ground beams & pad footings	15	15	0%	09-Apr-27	30-Apr-27	0
A1380	Ground slab - pours 1 & 2	12	12	0%	04-May-27	19-May-27	0
A1390	Ground slab curing	5	5	0%	20-May-27	26-May-27	0
RC2-SAMPLE.5.2 Structure		50	50	0%	27-May-27	04-Aug-27	0
A1400	Erect steel frame - Level 1	10	10	0%	27-May-27	09-Jun-27	0
A1420	Level 2 slab - formwork, reo & pour	15	15	0%	10-Jun-27	30-Jun-27	0
A1430	Level 2 slab curing	5	5	0%	01-Jul-27	07-Jul-27	0
A1440	Erect steel frame - Level 2 & roof	12	12	0%	08-Jul-27	23-Jul-27	0
A1450	Install precast panels - Level 2	8	8	0%	26-Jul-27	04-Aug-27	0
RC2-SAMPLE.5.3 Envelope		20	20	0%	05-Aug-27	01-Sep-27	0
A1480	Windows & external glazing	20	20	0%	05-Aug-27	01-Sep-27	0
A1490	Building A weathertight	0	0	0%		01-Sep-27	0
RC2-SAMPLE.5.5 Fit-out Level 1		15	15	0%	02-Sep-27	22-Sep-27	0
A1560	Internal framing & insulation - L1	15	15	0%	02-Sep-27	22-Sep-27	0
RC2-SAMPLE.5.6 Fit-out Level 2		35	35	0%	23-Sep-27	11-Nov-27	0
A1640	Internal framing & insulation - L2	15	15	0%	23-Sep-27	14-Oct-27	0
A1650	Plasterboard & set - L2	20	20	0%	15-Oct-27	11-Nov-27	0
RC2-SAMPLE.6 Building B - Administration		15	15	0%	12-Nov-27	02-Dec-27	0
RC2-SAMPLE.6.3 Fit-out		15	15	0%	12-Nov-27	02-Dec-27	0
A1770	Plasterboard & ceilings	15	15	0%	12-Nov-27	02-Dec-27	0
RC2-SAMPLE.7 Building C - Multipurpose Hall		40	40	0%	03-Dec-27	18-Feb-28	0
RC2-SAMPLE.7.3 Fit-out		40	40	0%	03-Dec-27	18-Feb-28	0
A1850	Acoustic wall linings	15	15	0%	03-Dec-27	13-Jan-28	0
A1870	Stage, AV & operable wal	15	15	0%	14-Jan-28	04-Feb-28	0
A1880	Services fit-off	10	10	0%	07-Feb-28	18-Feb-28	0
RC2-SAMPLE.9 Testing, Commissioning & Handover		25	25	0%	21-Feb-28	24-Mar-28	0
A1990	Testing & commissioning - Buildings B & C	15	15	0%	21-Feb-28	10-Mar-28	0
A2000	Defects inspection & rectification - B, C & externals	10	10	0%	13-Mar-28	24-Mar-28	0
A2030	As-built, O&M manuals & training	10	10	0%	13-Mar-28	24-Mar-28	0

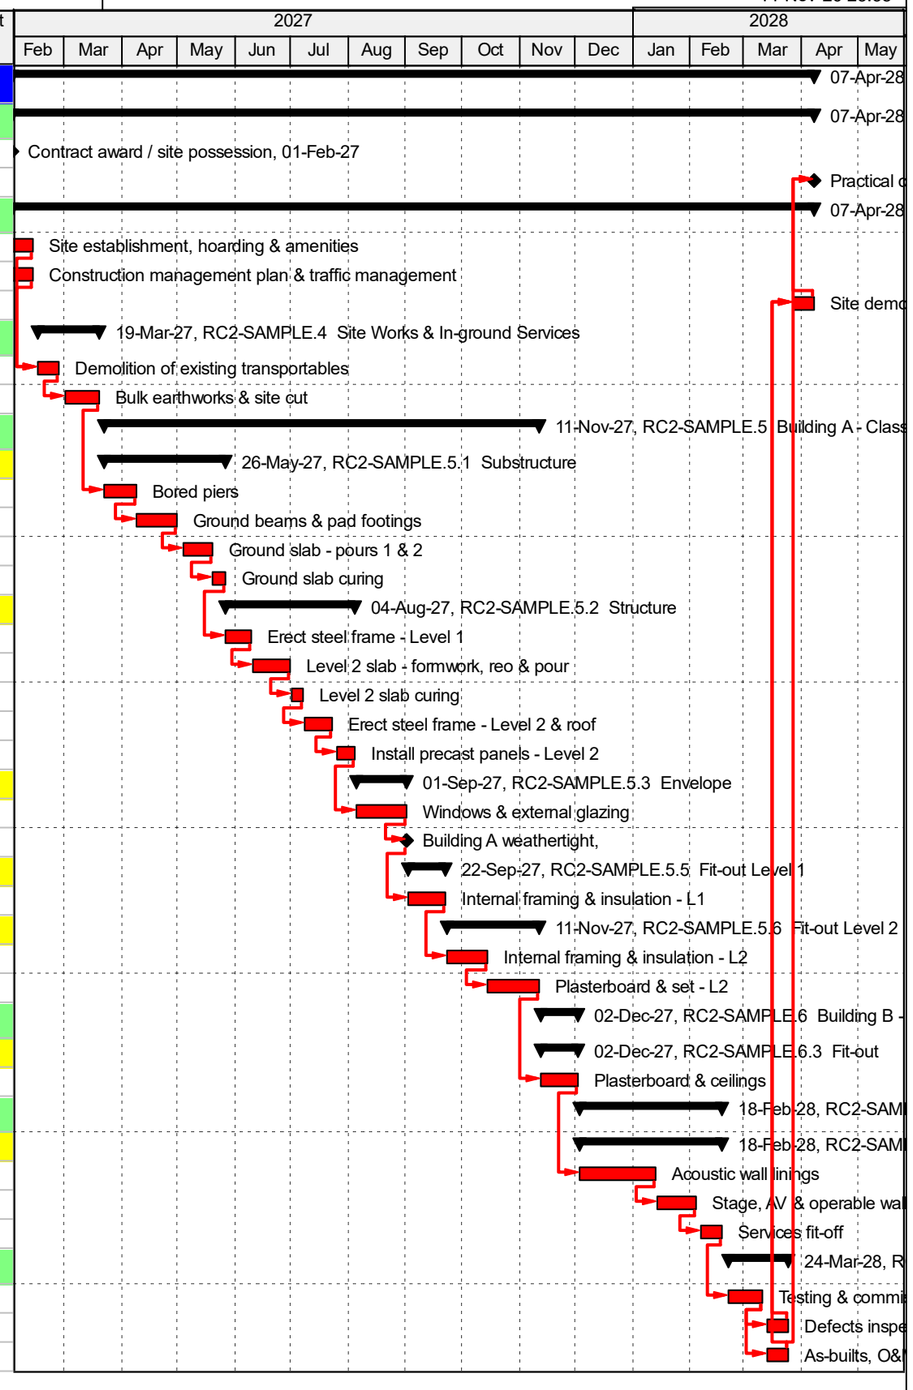

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: Critical.

© Oracle Corporation
