

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float
RC2-SAMPLE	**Riverside College Stage 2 (Sample)**	289	289	0%	01-Feb-27	07-Apr-28	0
RC2-SAMPLE.1	**Key Milestones**	289	289	0%	01-Feb-27	07-Apr-28	0
A1000	Contract award / site possession	0	0	100%	01-Feb-27		0
A1010	SP1 Practical completion - Building A	0	0	0%		17-Mar-28	15
A1020	SP2 Practical completion - Buildings B & C, externals	0	0	0%		31-Mar-28	5
A1030	Practical completion - whole of works	0	0	0%		07-Apr-28	0
RC2-SAMPLE.2	**Preliminaries & Approvals**	289	289	0%	01-Feb-27	07-Apr-28	0
A1040	Site establishment, hoarding & amenities	10	10	0%	01-Feb-27	12-Feb-27	0
A1050	Service locating & tree protection	5	5	0%	01-Feb-27	05-Feb-27	5
A1060	Construction management plan & traffic management	10	10	0%	01-Feb-27	12-Feb-27	0
A1070	Building consent - Stage 2 (structure)	25	25	0%	01-Feb-27	05-Mar-27	10
A1080	Building consent - Stage 3 (fit-out)	30	30	0%	10-Jun-27	21-Jul-27	30
A1090	Authority applications - water, sewer & power connection	30	30	0%	01-Feb-27	12-Mar-27	17
A1100	Site demobilisation	10	10	0%	27-Mar-28	07-Apr-28	0
RC2-SAMPLE.3	**Design, Procurement & Long Lead**	209	209	0%	01-Feb-27	25-Nov-27	30
A1110	Shop drawings - structural steel	20	20	0%	01-Feb-27	26-Feb-27	24
A1120	Shop drawing approval - structural steel	5	5	0%	01-Mar-27	05-Mar-27	24
A1130	Precast panel design (supplier)	25	25	0%	01-Feb-27	05-Mar-27	33
A1140	Shop drawings - precast panels	15	15	0%	08-Mar-27	30-Mar-27	33
A1150	Shop drawing approval - precast panels	5	5	0%	31-Mar-27	06-Apr-27	33
A1160	Shop drawings - windows & glazing	15	15	0%	08-Mar-27	30-Mar-27	44
A1170	Shop drawing approval - windows & glazing	5	5	0%	31-Mar-27	06-Apr-27	44
A1180	Mechanical design & equipment selection	25	25	0%	09-Apr-27	17-May-27	42
A1190	Lift design & order	15	15	0%	05-Aug-27	25-Aug-27	46
A1200	Joinery shop drawings & approval	20	20	0%	02-Sep-27	29-Sep-27	25
A1210	Fabricate structural steel - Building A	30	30	0%	08-Mar-27	20-Apr-27	24
A1220	Fabricate portal frame steel - Building C	25	25	0%	29-Jul-27	01-Sep-27	25
A1230	Fabricate precast panels - Building A	35	35	0%	07-Apr-27	27-May-27	33
A1240	Manufacture windows & glazing	40	40	0%	07-Apr-27	03-Jun-27	44
A1250	Manufacture & deliver mechanical plant	40	40	0%	18-May-27	12-Jul-27	42
A1260	Manufacture & deliver lift	44	44	0%	26-Aug-27	27-Oct-27	46
A1270	Manufacture joinery	30	30	0%	30-Sep-27	11-Nov-27	25
A1280	Electrical design & switchboard drawings	20	20	0%	02-Sep-27	29-Sep-27	30
A1290	Main switchboard manufacture & delivery	40	40	0%	30-Sep-27	25-Nov-27	30
RC2-SAMPLE.4	**Site Works & In-ground Services**	151	151	0%	15-Feb-27	17-Sep-27	43
A1300	Demolition of existing transportables	10	10	0%	15-Feb-27	26-Feb-27	0
A1310	Bulk earthworks & site cut	15	15	0%	01-Mar-27	19-Mar-27	0
A1320	In-ground stormwater	15	15	0%	22-Mar-27	13-Apr-27	12
A1330	In-ground sewer & water	15	15	0%	22-Mar-27	13-Apr-27	12
A1340	Consumer mains & comms pit and pipe	10	10	0%	06-Sep-27	17-Sep-27	43
A1350	Retaining walls	15	15	0%	29-Jul-27	18-Aug-27	20
RC2-SAMPLE.5	**Building A - Classroom Block (2 levels)**	209	209	0%	22-Mar-27	04-Feb-28	10
RC2-SAMPLE.5.1	**Substructure**	44	44	0%	22-Mar-27	26-May-27	0
A1360	Bored piers	12	12	0%	22-Mar-27	08-Apr-27	0
A1370	Ground beams & pad footings	15	15	0%	09-Apr-27	30-Apr-27	0
A1380	Ground slab - pours 1 & 2	12	12	0%	04-May-27	19-May-27	0
A1390	Ground slab curing	5	5	0%	20-May-27	26-May-27	0
RC2-SAMPLE.5.2	**Structure**	52	52	0%	27-May-27	06-Aug-27	33
A1400	Erect steel frame - Level 1	10	10	0%	27-May-27	09-Jun-27	0

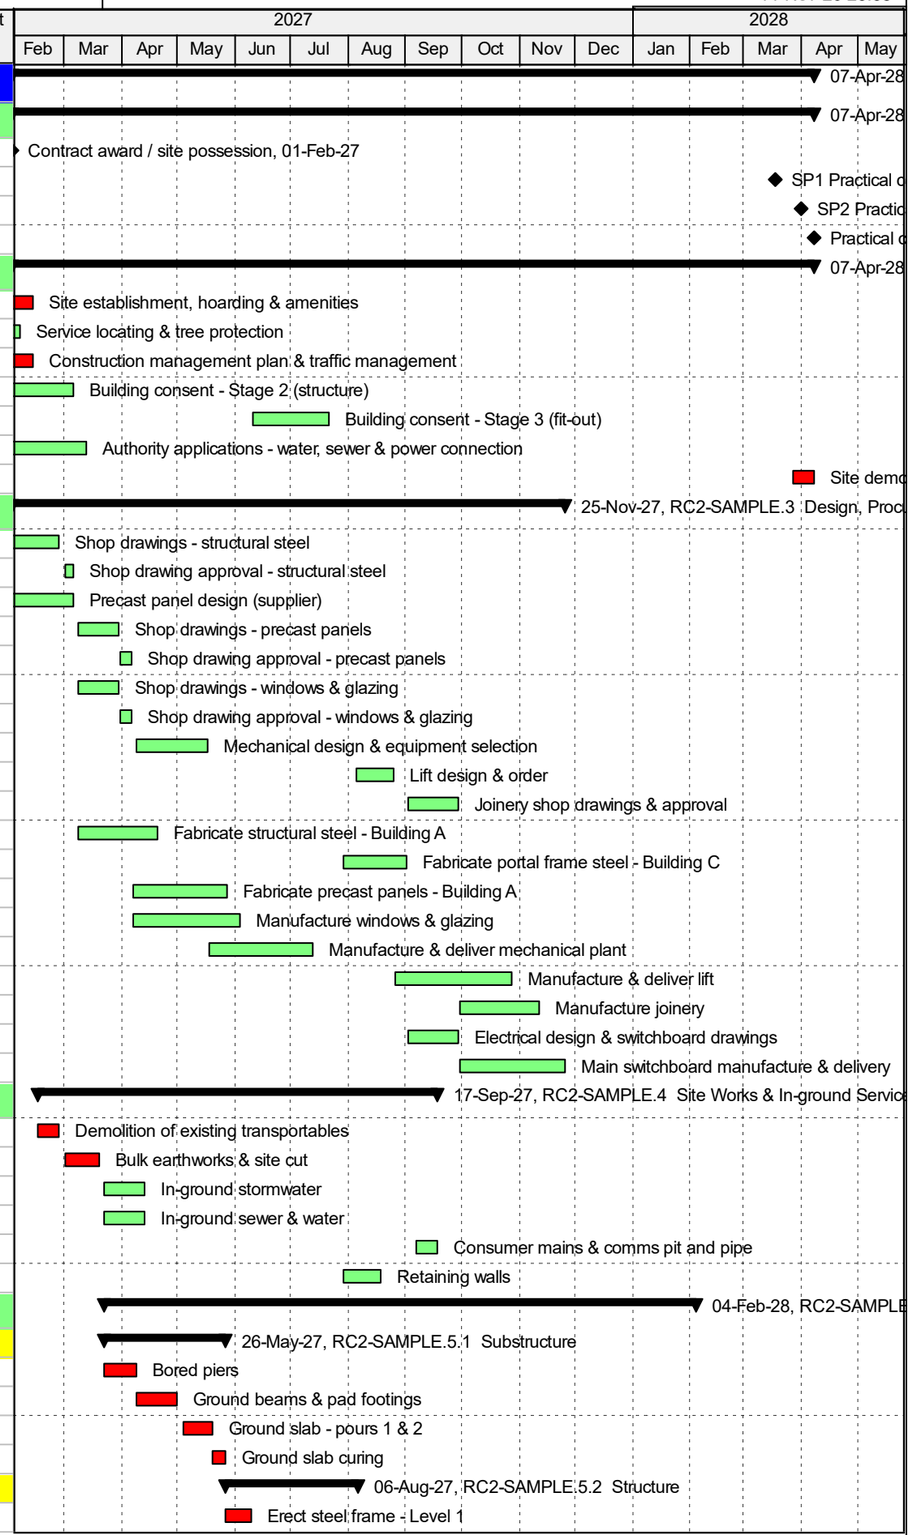

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float
A1410	Install precast panels - Level 1	8	8	0%	10-Jun-27	21-Jun-27	24
A1420	Level 2 slab - formwork, reo & pour	15	15	0%	10-Jun-27	30-Jun-27	0
A1430	Level 2 slab curing	5	5	0%	01-Jul-27	07-Jul-27	0
A1440	Erect steel frame - Level 2 & roof	12	12	0%	08-Jul-27	23-Jul-27	0
A1450	Install precast panels - Level 2	8	8	0%	26-Jul-27	04-Aug-27	0
A1460	Stairs & lift shaft	10	10	0%	26-Jul-27	06-Aug-27	33
RC2-SAMPLE.5.3 Envelope		28	28	0%	26-Jul-27	01-Sep-27	0
A1470	Roof sheeting, flashings & gutters	12	12	0%	26-Jul-27	10-Aug-27	16
A1480	Windows & external glazing	20	20	0%	05-Aug-27	01-Sep-27	0
A1490	Building A weathertight	0	0	0%		01-Sep-27	0
RC2-SAMPLE.5.4 Services Rough-in		90	90	0%	05-Aug-27	09-Dec-27	35
A1500	Mechanical rough-in	25	25	0%	05-Aug-27	08-Sep-27	25
A1510	Hydraulic rough-in	20	20	0%	02-Sep-27	29-Sep-27	10
A1520	Electrical & data rough-in	25	25	0%	05-Aug-27	08-Sep-27	25
A1530	Fire services rough-in	15	15	0%	02-Sep-27	22-Sep-27	15
A1540	Lift installation	20	20	0%	29-Oct-27	25-Nov-27	45
A1550	Main switchboard install & terminate	10	10	0%	26-Nov-27	09-Dec-27	30
RC2-SAMPLE.5.5 Fit-out Level 1		85	85	0%	02-Sep-27	20-Jan-28	20
A1560	Internal framing & insulation - L1	15	15	0%	02-Sep-27	22-Sep-27	0
A1570	Plasterboard & set - L1	20	20	0%	30-Sep-27	28-Oct-27	20
A1580	Ceilings - L1	12	12	0%	29-Oct-27	15-Nov-27	20
A1590	Joinery & fitments - L1	12	12	0%	16-Nov-27	01-Dec-27	23
A1600	Painting - L1	15	15	0%	16-Nov-27	06-Dec-27	20
A1610	Floor coverings - L1	10	10	0%	07-Dec-27	10-Jan-28	20
A1620	Services fit-off & lighting - L1	12	12	0%	16-Nov-27	01-Dec-27	33
A1630	Doors, hardware & signage - L1	8	8	0%	11-Jan-28	20-Jan-28	20
RC2-SAMPLE.5.6 Fit-out Level 2		80	80	0%	23-Sep-27	04-Feb-28	10
A1640	Internal framing & insulation - L2	15	15	0%	23-Sep-27	14-Oct-27	0
A1650	Plasterboard & set - L2	20	20	0%	15-Oct-27	11-Nov-27	0
A1660	Ceilings - L2	12	12	0%	12-Nov-27	29-Nov-27	3
A1670	Joinery & fitments - L2	12	12	0%	30-Nov-27	15-Dec-27	13
A1680	Painting - L2	15	15	0%	30-Nov-27	10-Jan-28	3
A1690	Floor coverings - L2	10	10	0%	11-Jan-28	24-Jan-28	10
A1700	Services fit-off & lighting - L2	12	12	0%	30-Nov-27	15-Dec-27	23
A1710	Doors, hardware & signage - L2	8	8	0%	25-Jan-28	04-Feb-28	10
RC2-SAMPLE.6 Building B - Administration		142	142	0%	08-Jul-27	15-Feb-28	3
RC2-SAMPLE.6.1 Substructure & Structure		30	30	0%	08-Jul-27	18-Aug-27	33
A1720	Pad footings & slab on ground	15	15	0%	08-Jul-27	28-Jul-27	20
A1730	Steel frame & roof structure	15	15	0%	29-Jul-27	18-Aug-27	33
RC2-SAMPLE.6.2 Envelope & Services		30	30	0%	19-Aug-27	29-Sep-27	30
A1740	Roof sheeting & cladding	12	12	0%	19-Aug-27	03-Sep-27	33
A1750	Windows & doors	10	10	0%	06-Sep-27	17-Sep-27	38
A1760	Services rough-in	15	15	0%	09-Sep-27	29-Sep-27	30
RC2-SAMPLE.6.3 Fit-out		52	52	0%	12-Nov-27	15-Feb-28	3
A1770	Plasterboard & ceilings	15	15	0%	12-Nov-27	02-Dec-27	0
A1780	Joinery & reception counter	10	10	0%	03-Dec-27	16-Dec-27	20
A1790	Painting & floor coverings	15	15	0%	11-Jan-28	01-Feb-28	3
A1800	Services fit-off	10	10	0%	02-Feb-28	15-Feb-28	3
RC2-SAMPLE.7 Building C - Multipurpose Hall		115	115	0%	19-Aug-27	18-Feb-28	0
RC2-SAMPLE.7.1 Substructure & Structure		25	25	0%	19-Aug-27	22-Sep-27	20

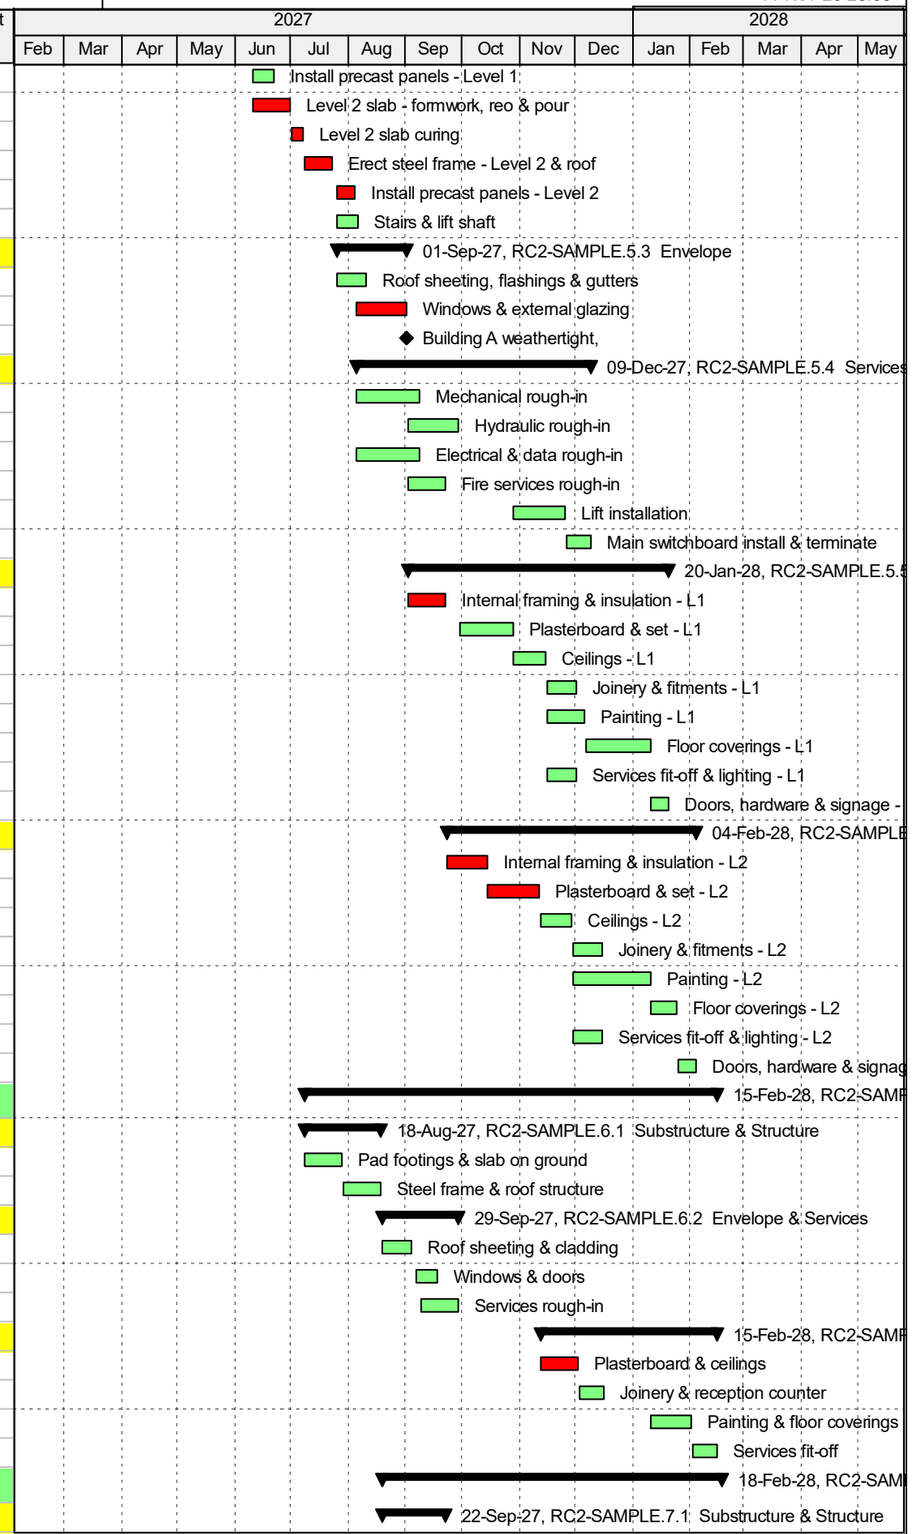


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float
A1810	Pad footings & slab on ground	15	15	0%	19-Aug-27	08-Sep-27	20
A1820	Erect portal frame	10	10	0%	09-Sep-27	22-Sep-27	20
RC2-SAMPLE.7.2 Envelope & Services		30	30	0%	23-Sep-27	04-Nov-27	20
A1830	Roof & wall cladding	15	15	0%	23-Sep-27	14-Oct-27	20
A1840	Services rough-in & mechanical plant	15	15	0%	15-Oct-27	04-Nov-27	20
RC2-SAMPLE.7.3 Fit-out		40	40	0%	03-Dec-27	18-Feb-28	0
A1850	Acoustic wall linings	15	15	0%	03-Dec-27	13-Jan-28	0
A1860	Sports flooring	12	12	0%	14-Jan-28	01-Feb-28	3
A1870	Stage, AV & operable wal	15	15	0%	14-Jan-28	04-Feb-28	0
A1880	Services fit-off	10	10	0%	07-Feb-28	18-Feb-28	0
RC2-SAMPLE.8 External Works & Landscaping		65	65	0%	15-Oct-27	04-Feb-28	25
A1890	Roads, kerbs & car park	20	20	0%	15-Oct-27	11-Nov-27	25
A1900	Paving & covered walkways	25	25	0%	12-Nov-27	16-Dec-27	25
A1910	Fencing & gates	10	10	0%	17-Dec-27	20-Jan-28	35
A1920	Landscaping & irrigation	20	20	0%	17-Dec-27	04-Feb-28	25
A1930	Play equipment & shade structures	15	15	0%	17-Dec-27	28-Jan-28	30
RC2-SAMPLE.9 Testing, Commissioning & Handover		65	65	0%	10-Dec-27	31-Mar-28	5
A1940	Authority connection & energisation of site supply	5	5	0%	10-Dec-27	16-Dec-27	30
A1950	Testing & commissioning - Building A	15	15	0%	07-Feb-28	25-Feb-28	10
A1960	Defects inspection & rectification - Building A	10	10	0%	28-Feb-28	10-Mar-28	15
A1970	Certificate of occupancy - Building A	5	5	0%	13-Mar-28	17-Mar-28	15
A1980	Building A handover	0	0	0%		17-Mar-28	15
A1990	Testing & commissioning - Buildings B & C	15	15	0%	21-Feb-28	10-Mar-28	0
A2000	Defects inspection & rectification - B, C & externals	10	10	0%	13-Mar-28	24-Mar-28	0
A2010	Certificate of occupancy - Buildings B & C	5	5	0%	27-Mar-28	31-Mar-28	5
A2020	Buildings B & C handover	0	0	0%		31-Mar-28	5
A2030	As-builts, O&M manuals & training	10	10	0%	13-Mar-28	24-Mar-28	0

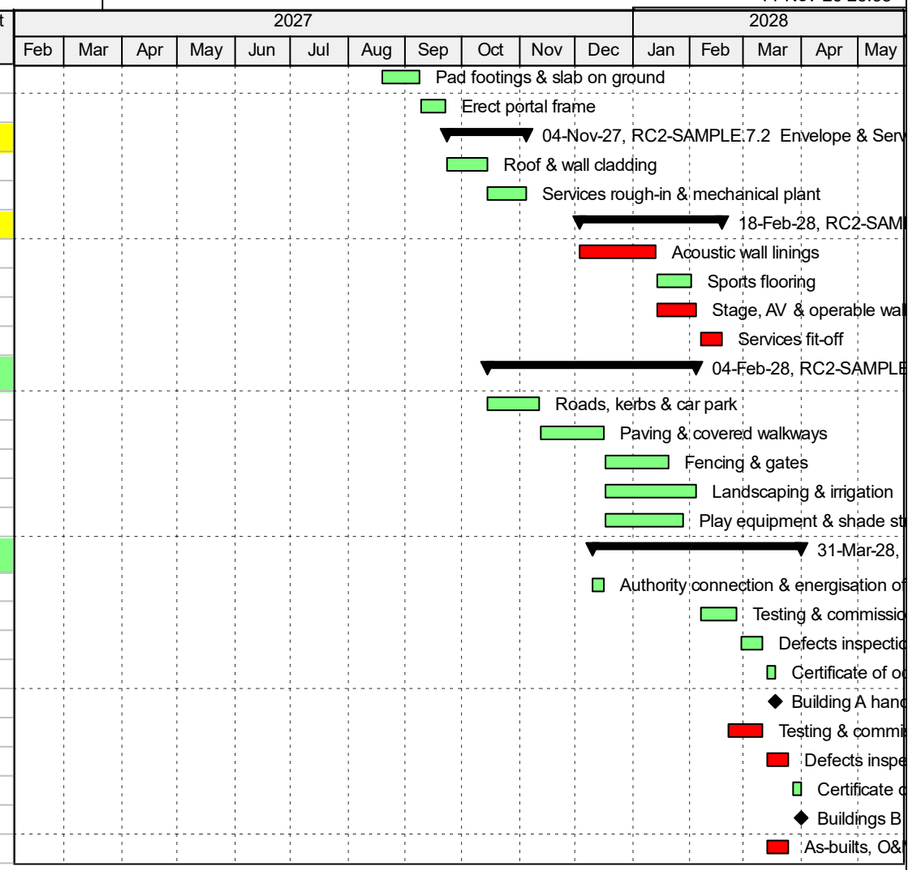

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation
